



May 9, 2023







Program Schedule Summary

5 Year Plan / Board Approved Projects

38*

Active Projects = 17
Completed Projects = 18
Not Started = 3

* Note that overall count has been reduced to reflect all 3000 series building projects (6) merged into one project.

Upcoming / Planned FMP Projects

17

Program Financial Summary

(February 2023 Month End)



\$363M Commitments


\$233M Expenditures





STATUS OF PROJECTS

COMMUNITY LEARNING CENTER

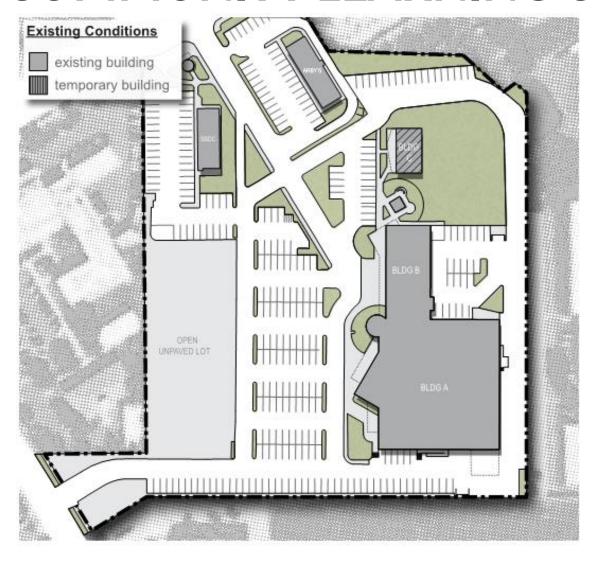






COMMUNITY LEARNING CENTER

COMMUNITY LEARNING CENTER	CURRENT PROJECT BUDGET	ANTICIPATED CONSTRUCTION START DATE	ANTICIPATED COMPLETION DATE	STATUS
Monument Sign and SBDC Demolition	\$1,051,443	Complete	Complete	COMPLETE
Arby's Building Demolition	\$122,245	Complete	Complete	COMPLETE
Building D (300) / New Student Services Building	\$12,305,973	Complete	Complete	COMPLETE
Parking Lot Renovation and Building C Demolition - PHASE I	\$254,000	Future	Future	COMPLETE
Building 100 & 200 Classrooms and Offices Renovation	\$12,671,405	Started - Spring 2021	Completed - Summer 2022	DSA CLOSEOUT
Community Learning Center Total =	\$26,405,066		20000	

SAN ELIJO CAMPUS

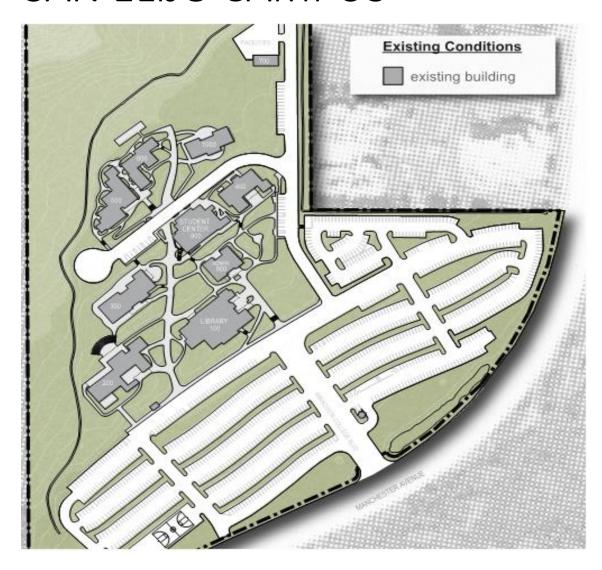





SAN ELIJO CAMPUS

	CURRENT PROJECT	ANTICIPATED	ANTICIPATED	
SAN ELIJO CAMPUS	BUDGET	CONSTRUCTION START DATE	COMPLETION DATE	STATUS
Building 600 Renovation	\$2,261,004	Complete	Complete	COMPLETE
Building 300 Renovation	\$2,678,463	Complete	Complete	COMPLETE
Building 500 Renovation	\$3,748,809	Complete	Complete	COMPLETE
Building 1100 New Student Services & Administration	\$13,980,978	Complete	Complete	COMPLETE
Building 200 Renovation	\$4,740,708	Complete	Complete	COMPLETE
Swing Space	\$2,916,709	Complete	Complete	COMPLETE
Underground Utilities Renovation	\$1,852,737	Complete	Complete	COMPLETE
Building 100 Library Renovation	\$6,083,064	Complete	Complete	COMPLETE
Building 900 Student Center Renovation	\$2,661,729	Complete	Complete	COMPLETE
Central Campus Quad Renovation and B800 Demo - PHASE I	\$649,416	Future	Future	COMPLETE
Building 400 Science Labs Renovation	\$4,798,886	Complete	Complete	COMPLETE
Miscellaneous Enhancements Project	\$1,312,616	Started - Summer 2022	Fall 2023	ONGOING
Building 700 Renovation	\$685,895	TBD	TBD	UPCOMING
San Elijo Campus Total =	\$48,371,014			

SAN ELIJO MISCELLANEOUS ENHANCEMENTS

• **Phase:** Design

Delivery Method: Design-Bid-Build


Current Budget: \$1.3M

• Designer: NV5

• Scope: This project included needed upgrades to SAN B200, B300, B600 and B900. The focus of building upgrades was to install metal wall caps at the top of perimeter walls to prevent moisture intrusion and do repairs to trellis structures. Installation of a new recycled water service for irrigation across campus is also being handled in this project.

 <u>Status:</u> Plans for the Recycled Water upgrades are under review with Olivenhain Water District and the SD County Health Department. CEQA Addendum processing will be going before May Board for approval.




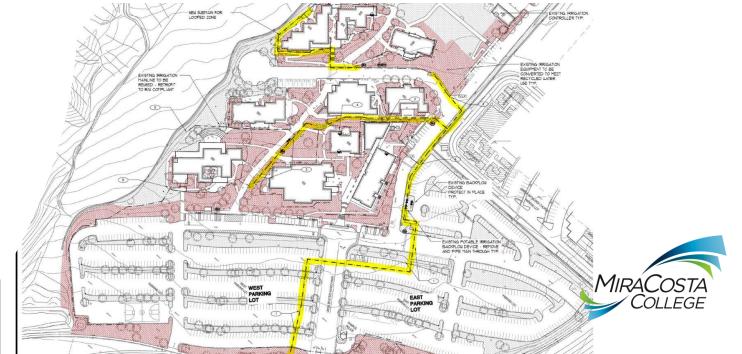


SAN ELIJO MISCELLANEOUS ENHANCEMENTS


Project Budget as of February 2023


Current Budget = \$1,312,616

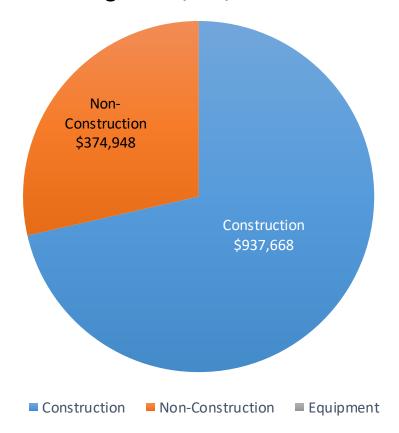

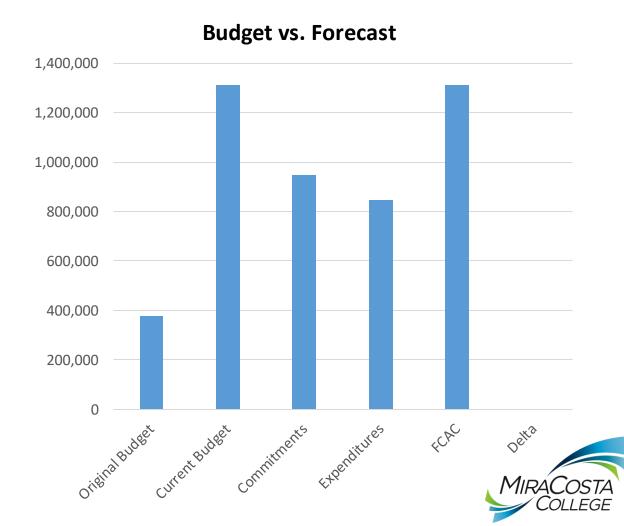

OCEANSIDE CAMPUS

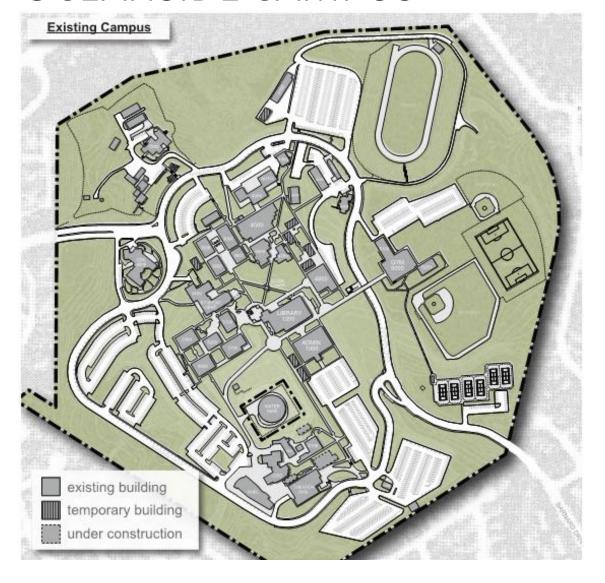

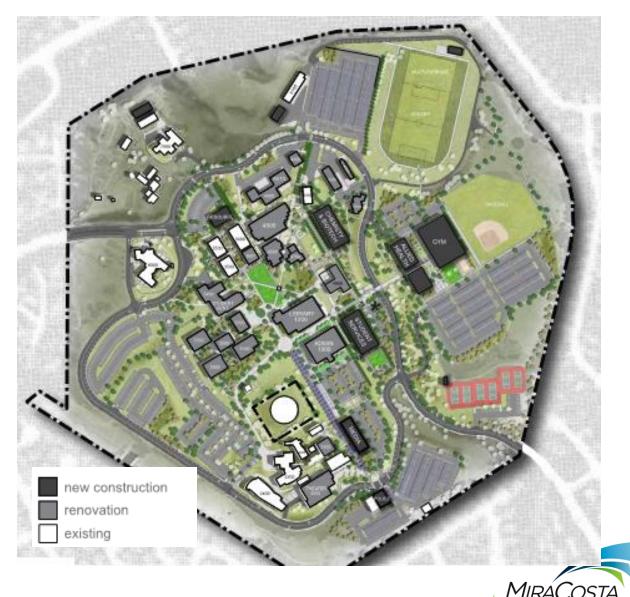

OCEANSIDE CAMPUS

OCEANSIDE CAMPUS	CURRENT PROJECT BUDGET	ANTICIPATED CONSTRUCTION START DATE	ANTICIPATED COMPLETION DATE	STATUS / PHASE
North Storm Drain Replacement	\$768,081	Complete	Complete	COMPLETE
Track and Field and Support Building Renovation	\$9,891,757	Complete	Complete	COMPLETE
New North Campus Parking Lot 4C Ex - PHASE I	\$205,512	Future	Future	COMPLETE
New Parking Lot 5A	\$13,609,435	Started - Spring 2021	Completed - Fall 2021	DSA CLOSEOUT
Strong Workforce Development Lab/ Trailer	\$950,000	Started - Summer 2021	Completed - Fall 2021	DSA CLOSEOUT
Building 1000 Administration Renovation	\$12,815,305	Started - Summer 2021	Completed - Spring 2023	DSA CLOSEOUT
Building 1400 New Student Services (includes Veterans)	\$62,064,022	Started - Summer 2021	Spring 2024	CONSTRUCTION
Building 5100 New Allied Health	\$29,763,333	Started - Spring 2022	Spring 2024	CONSTRUCTION
Building 5000 New Gymnasium Complex	\$41,372,096	Started - Spring 2022	Spring 2024	CONSTRUCTION
Building 1300 New Chemistry & Biotechnology	\$46,921,154	Fall 2022	Summer 2024	CONSTRUCTION
Building 2800 Media Arts Complex	\$25,859,673	Fall 2022	Fall 2024	CONSTRUCTION
Building 1200 Library Renovation	\$32,480,013	Spring 2023	Summer 2024	CONSTRUCTION

OCEANSIDE CAMPUS - Continued

OCEANSIDE CAMPUS	CURRENT PROJECT BUDGET	ANTICIPATED CONSTRUCTION START DATE	ANTICIPATED COMPLETION DATE	STATUS / PHASE
Communications Hub, Social Justice and Equity Centers. - Includes renovation of Buildings 3400 and 3700 - Includes a new building replacing 3000, 3100, 3200 and 3300	\$53,446,329	Fall 2024	Summer 2026	DESIGN
Wayfinding and Signage	\$290,000	TBD	TBD	DESIGN
Building 2000 Theatre Lighting	\$535,000	Summer 2023	Fall 2023	DESIGN
Campus Wide ADA Improvements	\$610,141	Ongoing	Ongoing	ONGOING
Campus Wide Utility Infrastructure Renovation	\$3,181,155	Ongoing	Ongoing	ONGOING
Swing Space	\$6,258,137	Ongoing	Ongoing	ONGOING
Monument Sign	\$167,512	TBD	TBD	UPCOMING
Building 4500 Science Renovation	\$33,346,062	TBD	TBD	UPCOMING
Oceanside Campus Total =	\$374,534,719			

OC B1000 ADMINISTRATION RENOVATION

Phase: Closeout

Delivery Method: Design-Bid-Build

Current Budget: \$11M

Architect: Little Architects

Building SQ FT: 18,800 SF


- Scope: The Administration Building will undergo a renovation to improve space efficiency and accessibility and replace failing infrastructure components. The existing mechanical, electrical, plumbing and structural systems will be replaced/upgraded to meet current building and seismic code requirements.
- Status: The Public Information Office portion of the building was finalized and is now in use. Final punch items are nearly complete.






OC B1000 ADMINISTRATION RENOVATION

Project Budget as of February 2023

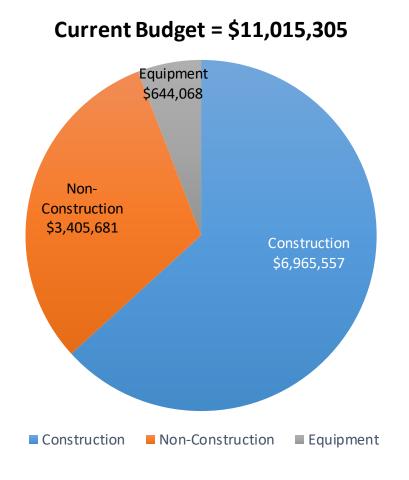

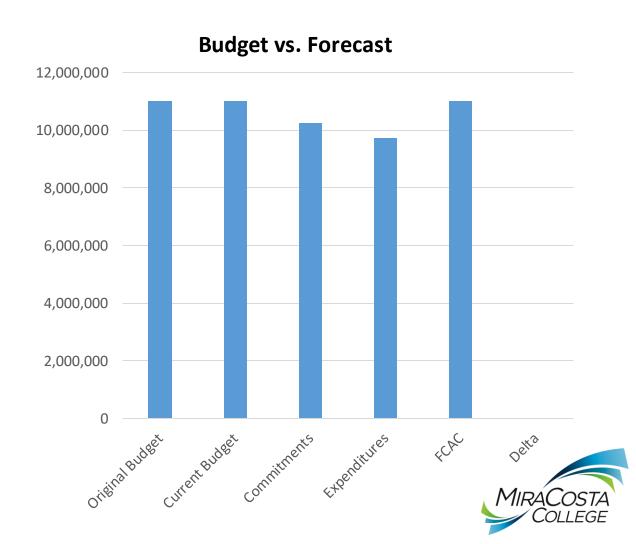

OC NEW KHAN BUILDING and GYM BUILDING

Phase: Construction

Delivery Method: Design-Build

Current Budget: \$41.4M

Criteria Architect: Lionakis

■ **DBE:** Balfour Beatty/HMC Architects

■ **Building SQ FT**: 40,915 SQ FT

 Scope: The new Gymnasium and the Kinesiology, Health and Nutrition Studies (KHAN) buildings will replace the existing gym buildings and provide a consolidated location for the new gymnasium, athletics instruction spaces, and the Wellness Center. The facility will also include locker rooms, equipment storage, and a multi-purpose studio.

 <u>Status</u>: This project is in a framing and rough in phase with extensive activity throughout the building and along the exterior.







OC NEW GYM BUILDING

Project Budget as of February 2023



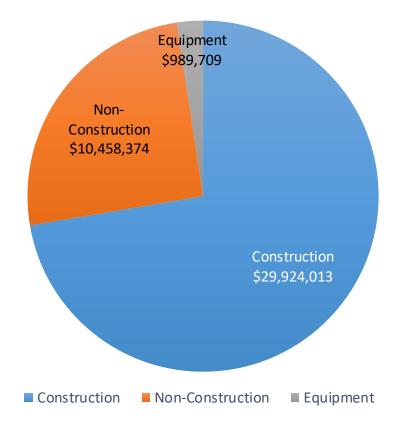

Budget vs. Forecast

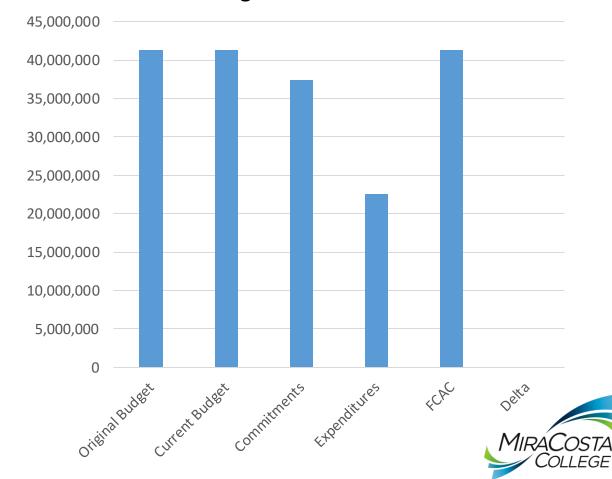

OC NEW ALLIED HEALTH BUILDING (Heyden Hall)

Phase: Construction

Delivery Method: Design-Build

Current Budget: \$29.8M

Criteria Architect: Lionakis

■ **DBE:** Balfour Beatty/HMC Architects

■ **Building SQ FT**: 25,251 SQ FT

Scope: A new facility will provide a consolidated location and appropriate facilities for all of the Allied Health programs. Programming includes state-of-theart simulation spaces, including patient and operating rooms, as well as hands-on skills labs and classrooms. The plan includes a single story building whose design is coordinated with the new gym complex to create a unified campus and design aesthetic.

Status: This project is in a framing and rough in phase with extensive activity throughout the building and on the exterior getting ready for cladding.







OC NEW ALLIED HEALTH BUILDING

Project Budget as of February 2023



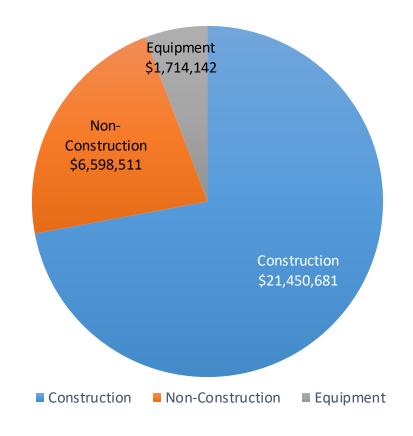

Budget vs. Forecast

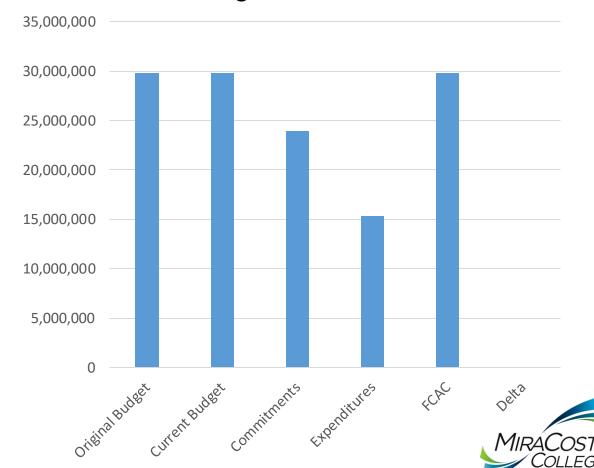

OC NEW STUDENT SERVICES BUILDING

Phase: Construction

Delivery Method: Design-Build

Current Budget: \$62.1M

Criteria Architect: Gensler

DBE: Swinerton / DLR

Building SQ FT: 54,556 SQ FT

Scope: The new Student Services facility will consolidate student service functions currently scattered throughout the campus to a single, one-stop shop, and will include a new home for the Veterans Center. Located in the former home of Pedley Park, the new building is strategically positioned to act as a gateway building for the campus, providing a much-needed sense of entry and easy wayfinding for new or prospective students. The building will be a two-story structure and will allow access and entry from the street level for visitors and campus promenade level for current students.


Status: Extensive rough in efforts are underway on the interior and as wall rough in is completed, drywall is being installed. The exterior is being prepared for stucco and metal panels. Continuing to work through challenges with switch gear and transformer lead times to minimize project impact.






OC NEW STUDENT SERVICES BUILDING

Project Budget as of February 2023

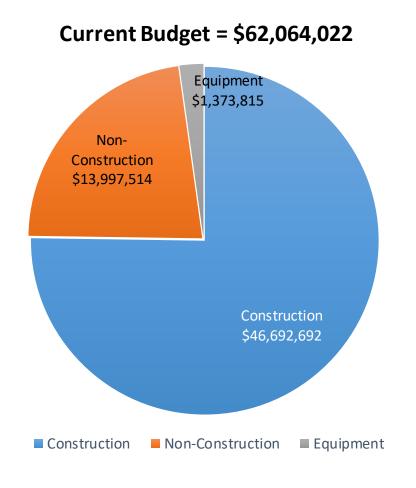

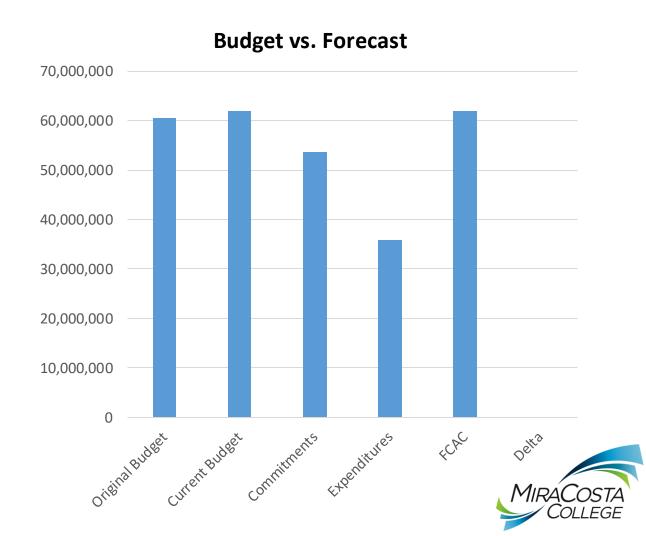

OC NEW CHEMISTRY & BIOTECHNOLOGY BUILDING

Phase: Construction

Delivery Method: Design-Build

Current Budget: \$46.9M

Criteria Architect: Lionakis

■ **DBE:** CW Driver / HED

■ **Building SQ FT**: 23,391 SQ FT

• Scope: The new Chemistry and Biotechnology Building will provide a state-of-the-art facility with new chemistry and biochemistry labs and two 40-seat flexible classrooms. As the district's Biotechnology program expands into a Baccalaureate degree program, the building will provide needed space for growth. The project will be the major component of the Science, Technology, Engineering and Mathematics (STEM) quad and plaza.


 <u>Status</u>: Foundation work was completed. Structural steel is currently being erected onsite.






OC NEW CHEMISTRY & BIOTECHNOLOGY BUILDING

Project Budget as of February 2023

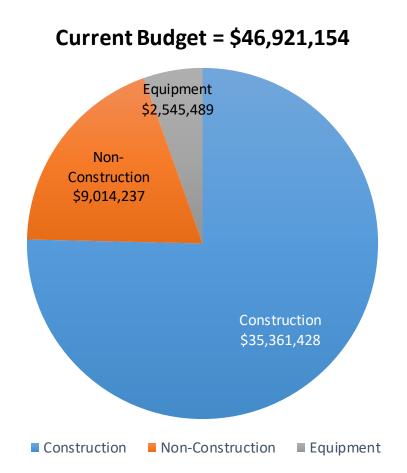

Budget vs. Forecast

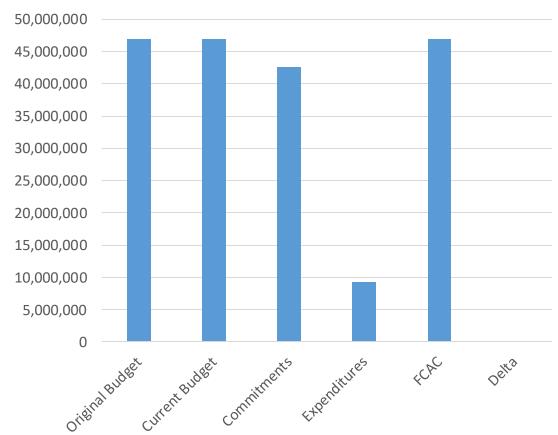



OC NEW MEDIA ARTS COMPLEX - BUILDING 2800

Phase: Construction

Delivery Method: Design-Build

Current Budget: \$25.9M

DBE: Balfour Beatty / HMC Architects

Building SQ FT: 10,471 SQ FT

Scope: The new Arts/Media Services Building will house a variety of functions, serving the students of the arts hub and the campus. It will include a new Art Gallery, two computer labs, a film studies classroom, student study and collaboration spaces, faculty offices, the Media Arts labs and extensive display areas for student art. It will provide dedicated student-friendly study and collaboration spaces. Proposed as a single-story facility, the building will have a strategic path of engagement to the campus promenade.


Status: Grading and utility work continues. The team is currently working on the underground retention system as well ADA compliance work with the sidewalk and bus stop along Barnard Ave.







OC NEW ARTS & MEDIA BUILDING

Project Budget as of February 2023



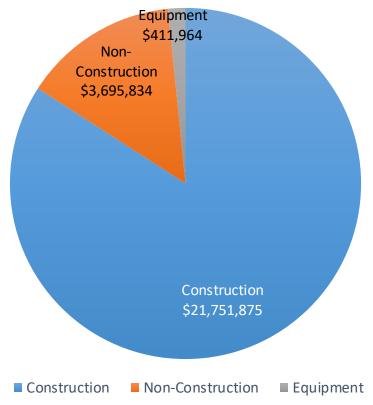

Budget vs. Forecast

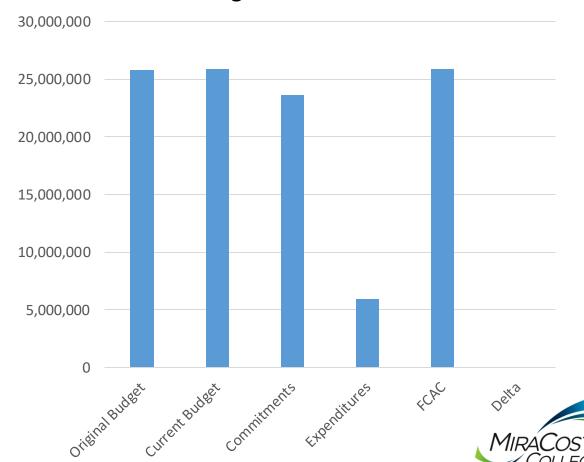

OC B1200 LIBRARY RENOVATION

Phase: Construction

• **Delivery Method:** Design-Build


Current Budget: \$32.5M

■ **DBE**: Level 10/ Mosher Drew

■ **Building SQ FT**: 47,790 SQ FT

be undergoing a full renovation to upgrade mechanical, electrical and plumbing systems within the building. Interior layouts will be adjusted to accommodate changing programming needs of the building. Addressing acoustic concerns is a key feature.

 Status: Framing has been quickly progressing on the interior and trades have been completing overhead rough in and commencing in wall work where possible. Work continues on the exterior with the revisions to the entry space.

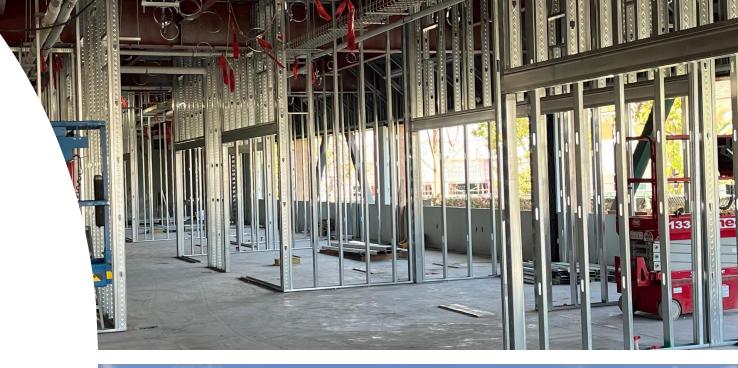





OC NEW LIBRARY BUILDING

Project Budget as of February 2023



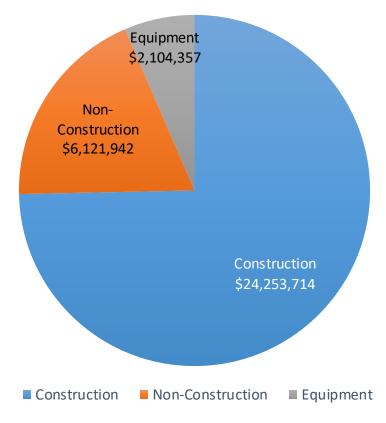

Budget vs. Forecast

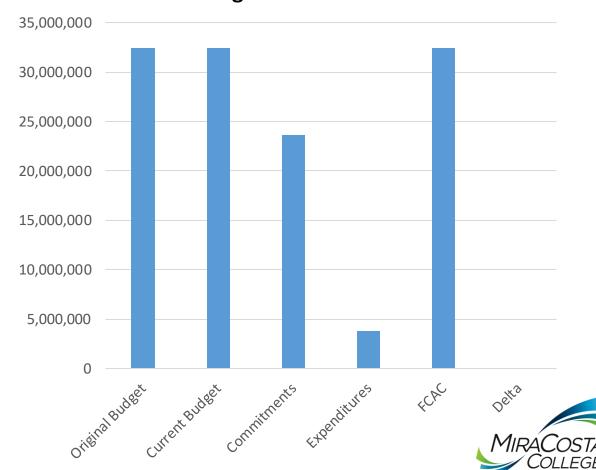

OC 3000 SERIES RENOVATION

Phase: Design

Delivery Method: Design-Build

Current Budget: \$53.4M

■ **DBE:** Rudolph & Sletten / Gensler


■ **Building SQ FT**: 56,098 SQ FT


- Scope: This expansive project consists of renovating buildings 3400 and 3700, and replacing (4) aging buildings; 3000, 3100, 3200 and 3300. This will form a Communications Hub and create a cohesive space for the Social Justice and Equity Centers and provide for renovations to the existing Student Center. The scope will include classroom, office, study, and student group collaboration spaces.
- <u>Status</u>: Schematic Design phase work has begun with focus on the Communications Hub. Meetings for User group input are continuing.



3000 SERIES RENOVATION

Project Budget as of February 2023

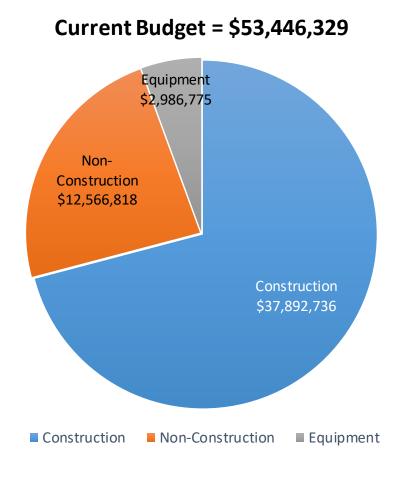

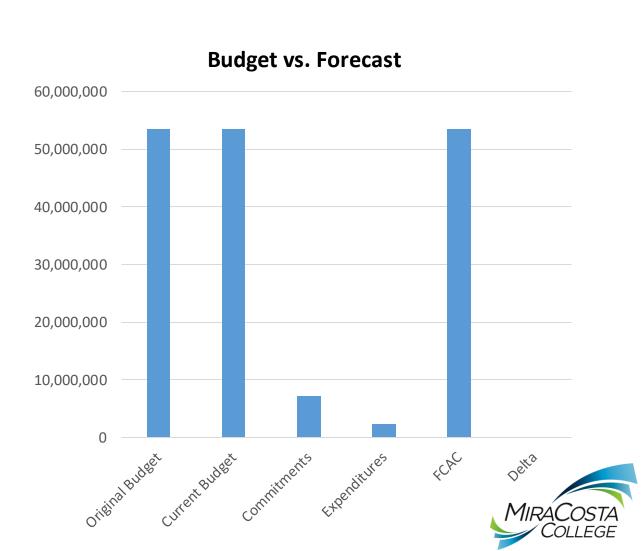

OC Wayfinding and Signage

Phase: Design


Delivery Method: TBD

Current Budget: \$290K

Architect: DLR


Location: Campuswide


- Scope: This planning project is taking a comprehensive look at wayfinding and signage needs across the Oceanside Campus to develop a functional and effective standardized signage plan. This includes both vehicular and pedestrian wayfinding, interior and exterior signage and monument/entry signage. Final designs would be rolled out in active construction projects or future projects as it applies.
- Status: Design efforts are nearly complete for an updated Oceanside Signage Standard. The team is moving forward on a design for biddable plans to implement signage updates across campus. Additionally, the team is working to do "street view" mapping of the campuses starting with San Elijo.

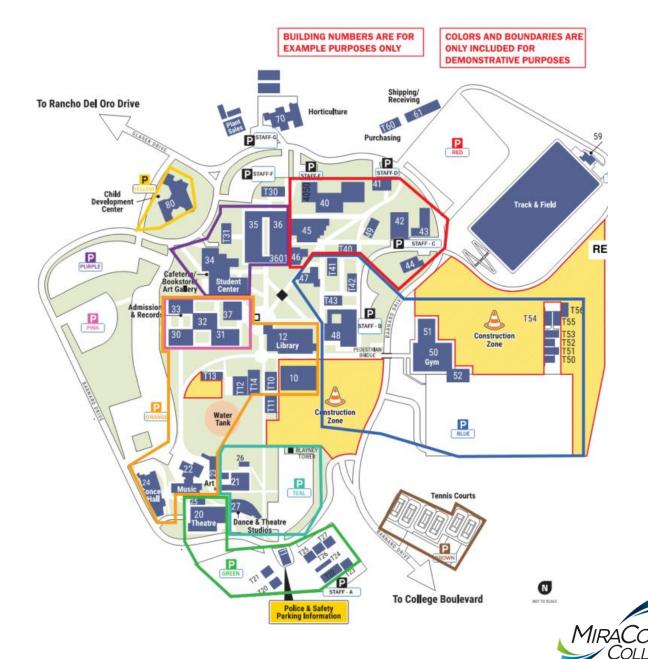

OC Wayfinding and Signage

Project Budget as of February 2023

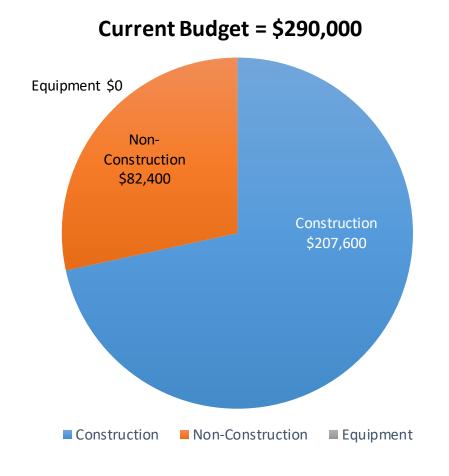

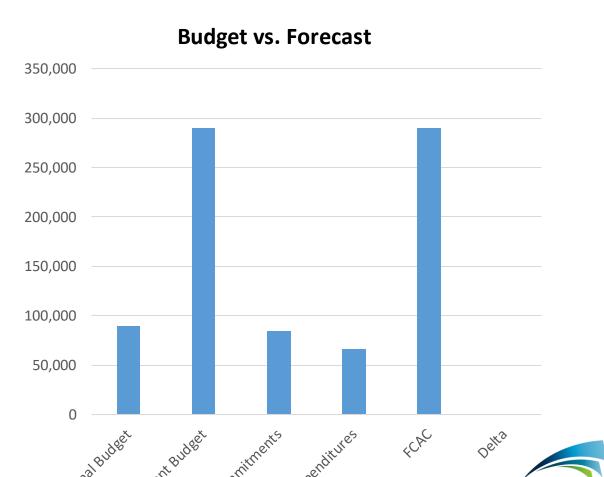



STATUS OF CONTRACTS LET

STATUS OF CONTRACTS LET – Upcoming

- Design-Build Request for Qualifications/Proposals (RFQ/Ps)
 - > 4500 Building RFQ/P upcoming
- Request for Task Order Proposals (RFTOPs)
- None





STATUS OF FINANCE

STATUS OF FINANCE

Master Program Budget – As of February 2023 Month End

- > See attached report
- > Commitments \$363M
- > Expenditures \$233M





Questions
